



# CTL

## CERTIFIED TESTING LABORATORIES, INC.

### PROCTOR DATA SHEET - NYC BC 1705.6

**CLIENT:** Metro Green

**DATE:** 2/9/26

**LAB#:** 16257

**PROJECT:** Metro Green Yard stockpile Item 4

**TIME IN:** 9:00 am

**TIME OUT:** 3:00 pm

**WEATHER:** 73 F

**CONTRACTOR:** Metro Green

**TECHNICIAN:** Dale Joseph


**QUALIFICATION:** ACI #949971

**ARCHITECT/ENGINEER:** N/A

A) Weight of wet soil and mold	12.97lb	13.33lb	13.44lb	
B) Weight of mold	9.3lb	9.3lb	9.3lb	
C) Weight of soil (A-B)	3.67lb	4.03lb	4.14lb	
D) Wet density Cx30 for 4" mold Cx13.33 for 6" mold	110.1	120.9	124.2	
E) Weight of Wet Soil and Tare pan	380	396	440	
F) Weight of dry soil and Tare pan	366	374	402	
G) Weight of Tare Pan	226.0	226.0	226.0	
H) Weight of water – (E-F)	14	22	38	
I) Weight of dry soil (F-G)	140	148	176	
J) Moisture Content	10.0	14.86	21.6	
K) Dry density	100.1	105.3	102.1	
L) Proctor from curves		107.4 @	16.2%	
N) Final Proctor (L+M)				

Equipment Used: Soils Kit SN

VS/ dk



Respectfully Submitted,  
CERTIFIED TESTING LABORATORIES, INC  
Vladimir Sirota, P.E.

CTL SOF-6  
12/22/2023  
KD


All reports are the confidential property of clients, and information contained may not be published or reproduced, pending our written approval.

140 Marbledale Road, Tuckahoe, NY 10707 | (718) 824-1616 |  
infobronx@certifiedtestinglabs.com

PHOTO NO.: 1

CLIENT: Metro Green

PROJECT: Yard stockpile Item 4

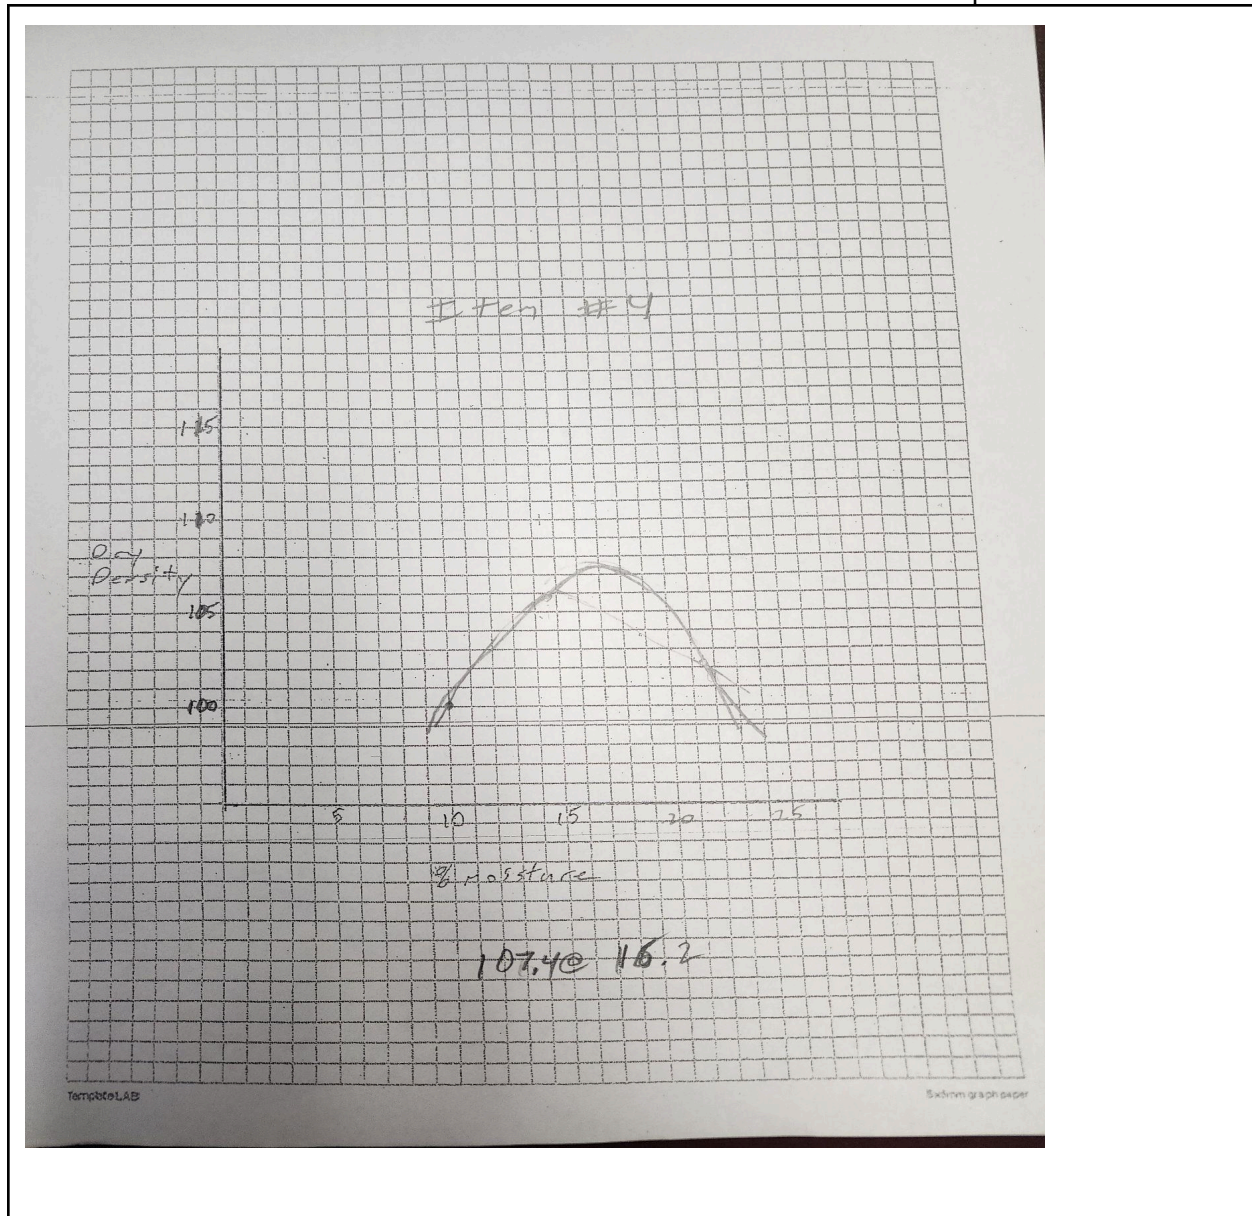

PICTURE OF: Proctor graph

FLOOR: N/A

LOCATION ON FLOOR: N/A

DATE: 2/9/26

All reports are the confidential property of clients, and information contained may not be published or reproduced, pending our written approval.

140 Marbledale Road, Tuckahoe, NY 10707 | (718) 824-1616 |

infobronx@certifiedtestinglabs.com
